DRAFT SCHEDULE IMPLEMENTING COHO SALMON INCIDENTAL TAKE REGULATIONS

ID	Task Name	Duration	Start	Finish	Predecessors
1	Director's Approval of draft regu	1 day?	Mon 7/3/06	Mon 7/3/06	
2	Prepare RFQ for CEQA consult	20 days	Wed 7/5/06	Tue 8/1/06	1
3	Circulate RFP to potential cons	15 days	Wed 8/2/06	Tue 8/22/06	2
4	Interview/select consultant	15 days	Wed 8/23/06	Wed 9/13/06	3
5	Finalize contract and approve	60 days	Thu 9/14/06	Tue 12/12/06	4
6	Prepare IS and NOP	30 days	Wed 12/13/06	Fri 1/26/07	5
7	CEQA Scoping/APA Pre-notice	60 days	Mon 1/29/07	Tue 4/24/07	6
8	Public scoping meeting	0 days	Tue 2/20/07	Tue 2/20/07	7SS+15 days
9	Develop regulatory package	60 days	Wed 2/21/07	Tue 5/15/07	7SS+15 days
10	Develop DEIR	60 days	Wed 2/21/07	Tue 5/15/07	8SS
11	Notice of Proposed Rulemaking	0 days	Tue 5/15/07	Tue 5/15/07	10
12	Notice of Completion and DEIR	0 days	Tue 5/15/07	Tue 5/15/07	11SS
13	APA and CEQA Public Comme	35 days	Wed 5/16/07	Thu 7/5/07	12
14	Public Hearing	0 days	Wed 6/13/07	Wed 6/13/07	13SS+20 days
15	Prepare responses to comment	30 days	Fri 7/6/07	Thu 8/16/07	13
16	Prepare final rulemaking	30 days	Fri 7/6/07	Thu 8/16/07	13
17	Prepare FEIR	40 days	Fri 7/6/07	Thu 8/30/07	13
18	Prepare APA Notice of Propose	15 days	Fri 7/6/07	Thu 7/26/07	16SS
19	Finalize Rulemaking Package	15 days	Fri 7/27/07	Thu 8/16/07	18
20	Finalize FEIR	15 days	Fri 7/27/07	Thu 8/16/07	19SS
21	Prepare Notice of Completion	10 days	Fri 8/17/07	Thu 8/30/07	20
22	File Notice of Completion	0 days	Fri 9/7/07	Fri 9/7/07	21FS+5 days
23	Certify FEIR	0 days	Fri 9/7/07	Fri 9/7/07	22SS
24	Approve Project/Make CEQA F	15 days	Mon 9/10/07	Fri 9/28/07	22SS
25	File Notice of Determination	0 days	Tue 10/2/07	Tue 10/2/07	24FS+2 days
26	File Copies of FEIR with Respo	10 days	Mon 10/1/07	Mon 10/15/07	24
27	Assemble Rulemaking File	10 days	Tue 10/16/07	Mon 10/29/07	26
28	OAL Review	30 days	Tue 10/30/07	Thu 12/13/07	27
29	File with Secretary of State	10 days	Fri 12/14/07	Fri 12/28/07	28
30	Regulations Effective	21 days	Tue 1/1/08	Tue 1/29/08	29FS+1 day

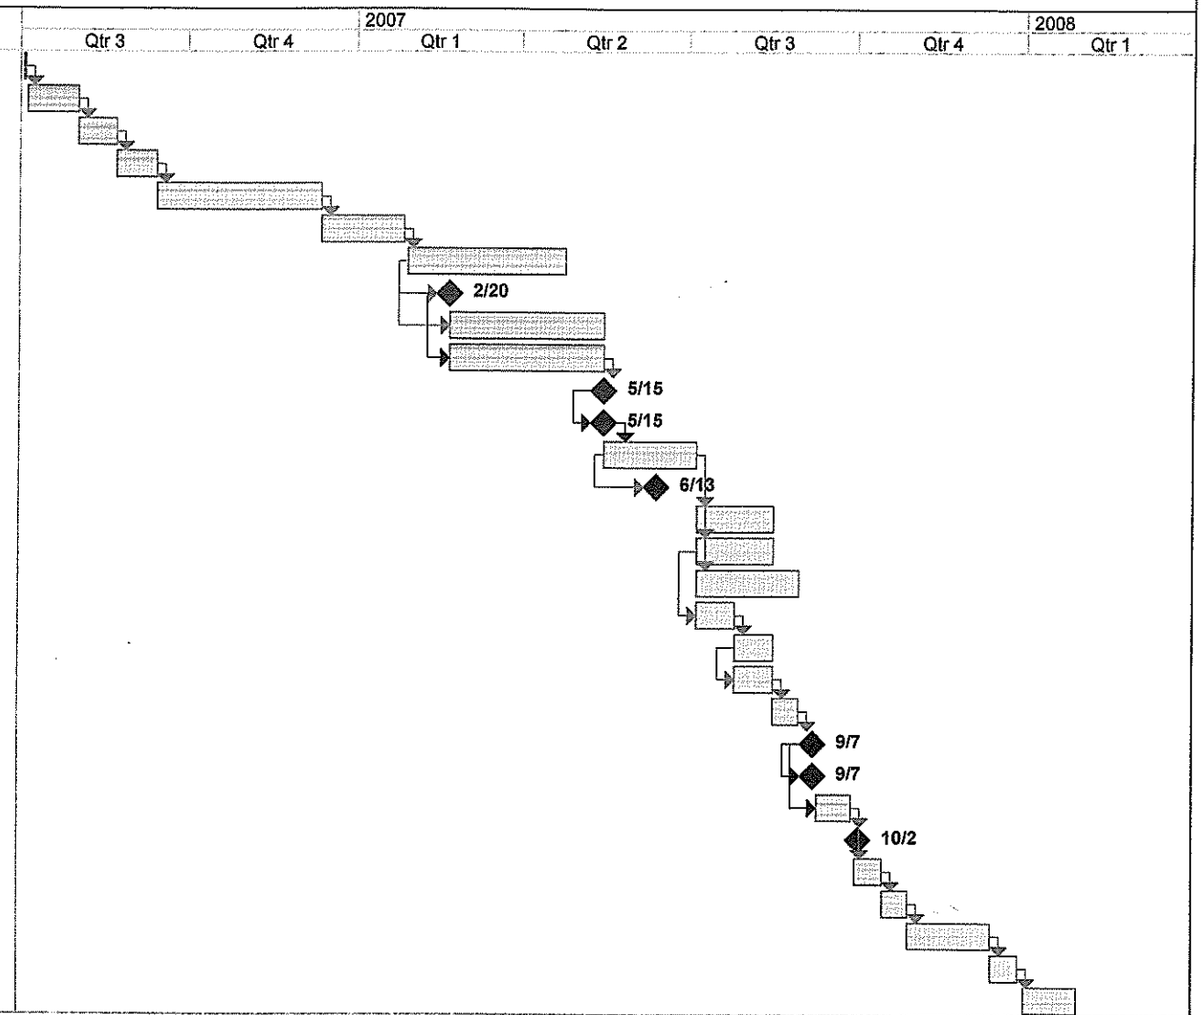

Project: DRAFT 2112 workplan.mpp
Date: Tue 5/16/06

Task | Progress | Summary | External Tasks | Deadline
Split | Milestone | Project Summary | External Milestone

RECEIVED
JUL 1 2 2006
